


Castle Street Improvement Works Update

We are continuing to make good progress across multiple phases of the Castle Street Improvement Works. Over the coming fortnight, works will focus on new paving, drainage infrastructure, kerb installation, street lighting, and traffic signal infrastructure as we continue to transform the area and improve the public realm for residents, businesses, and visitors.

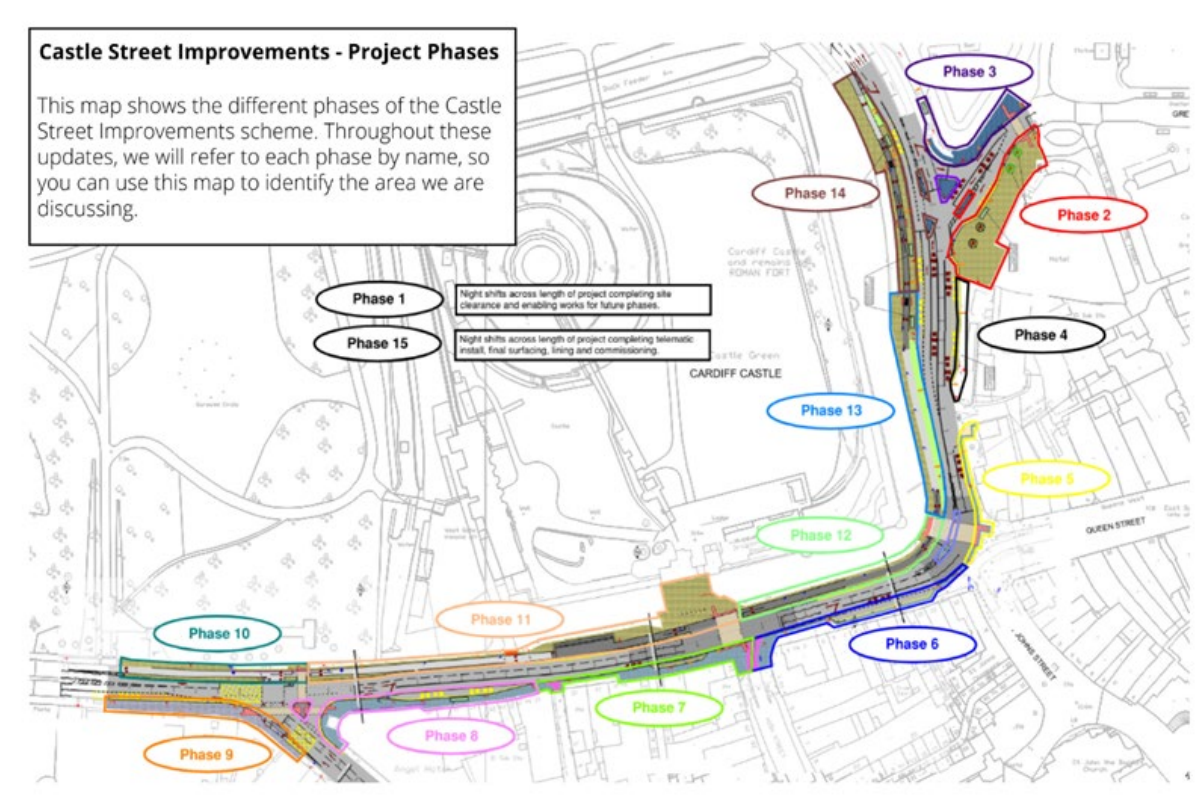

Progress Update

- **Phase 2** – Preparatory works and installation of new pennant paving slabs are continuing, progressing towards the main entrance of the Hilton Hotel.
- **Phase 3** – Ducting installation is ongoing. We are also progressing with the installation of new drainage infrastructure and will shortly begin constructing new kerb lines.
- **Phase 6** – Underground civil engineering works, including kerb installation, lighting column foundations, and new street signage, are nearing completion. Installation of new paving slabs is continuing westbound towards St Mary's Street.
- **Phase 7** – Traffic management will be mobilised into this phase on 7 September, enabling works to commence in this area.


- **Phase 8** – Installation of new kerb lines is continuing westbound and around the corner onto Westgate Street. Works in this area also include the installation of signposts, lighting columns, traffic signal ducting, and loop detectors.

Upcoming Night Works

To safely undertake essential highway improvement works and minimise disruption to daytime traffic, a programme of night works is scheduled between Monday 24 August and Thursday 27 August.

Works will take place between 11:30pm and 5:00am each night and will include:

- Installation and removal of temporary traffic management each night to create a safe working area.
- Removal of existing kerbs.
- Installation of new kerb lines.
- Installation of traffic signal ducting and loop detector chambers.

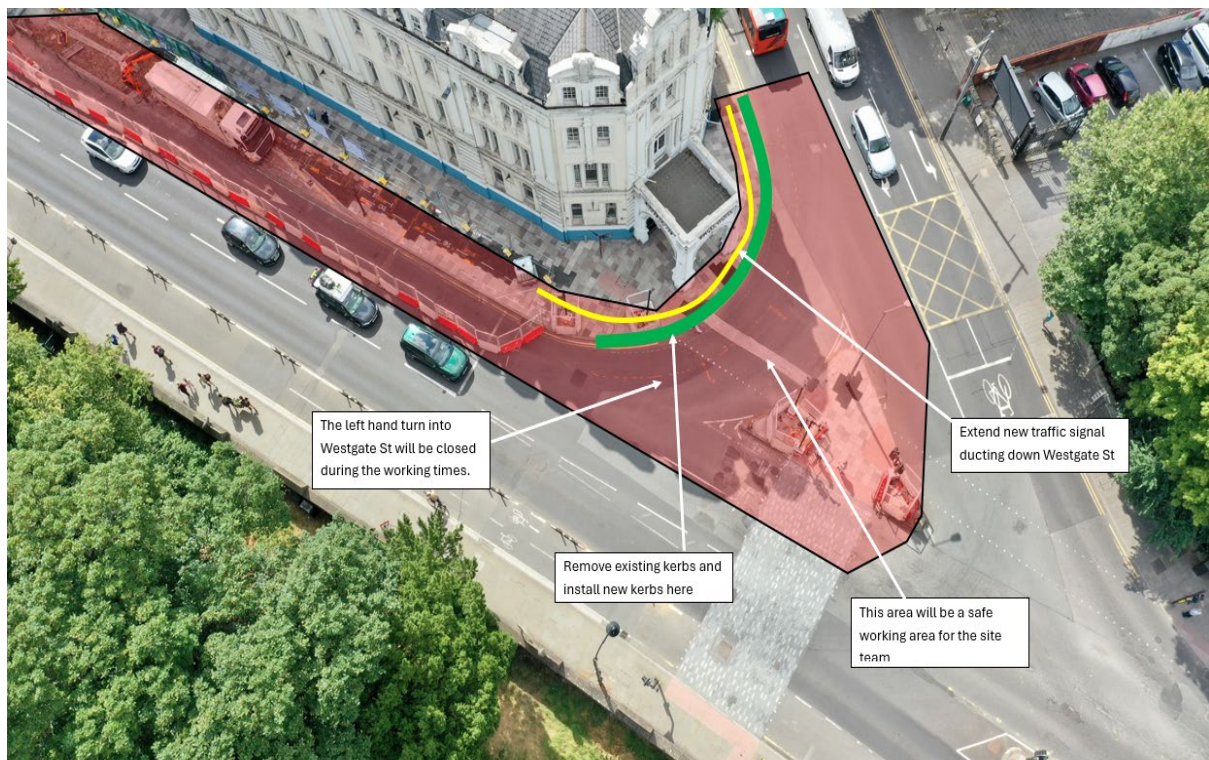

The left-turn lane into Westgate Street will be reopened at the end of each shift, and the road will be fully reopened by 5:00am each morning.

While every effort will be made to minimise disturbance, some noise is unavoidable during these works. Due to traffic volumes and safety requirements, these activities cannot be undertaken during normal daytime hours when the carriageway remains open to traffic.

We apologise for any inconvenience this may cause and thank residents, businesses, and road users for their continued patience and cooperation while these important improvements are delivered. Further updates will be provided as the project progresses.

Get in Touch

If you have any questions or concerns about the Castle Street Improvements, please contact us:

Email: talktous@hotmail.co.uk

Public Liaison: 07977 091261

Next Update: Our next fortnightly e-bulletin will be issued Friday 4 September.
