

Castle Street Improvements – Fortnightly Update


Welcome to our latest Castle Street Improvements e-bulletin.

We're pleased to share another update on the progress being made across the scheme. Thank you to everyone who continues to support the project as we work to create a safer, more accessible and more attractive city centre for residents, businesses and visitors.

Over the next two weeks, our team will be progressing works across several phases of the project, with activities including paving, drainage, road construction and traffic signal improvements.

What's Happening Over the Next Two Weeks

Our works continue to progress across several phases of the scheme. Below is an overview of the activities planned over the next fortnight.

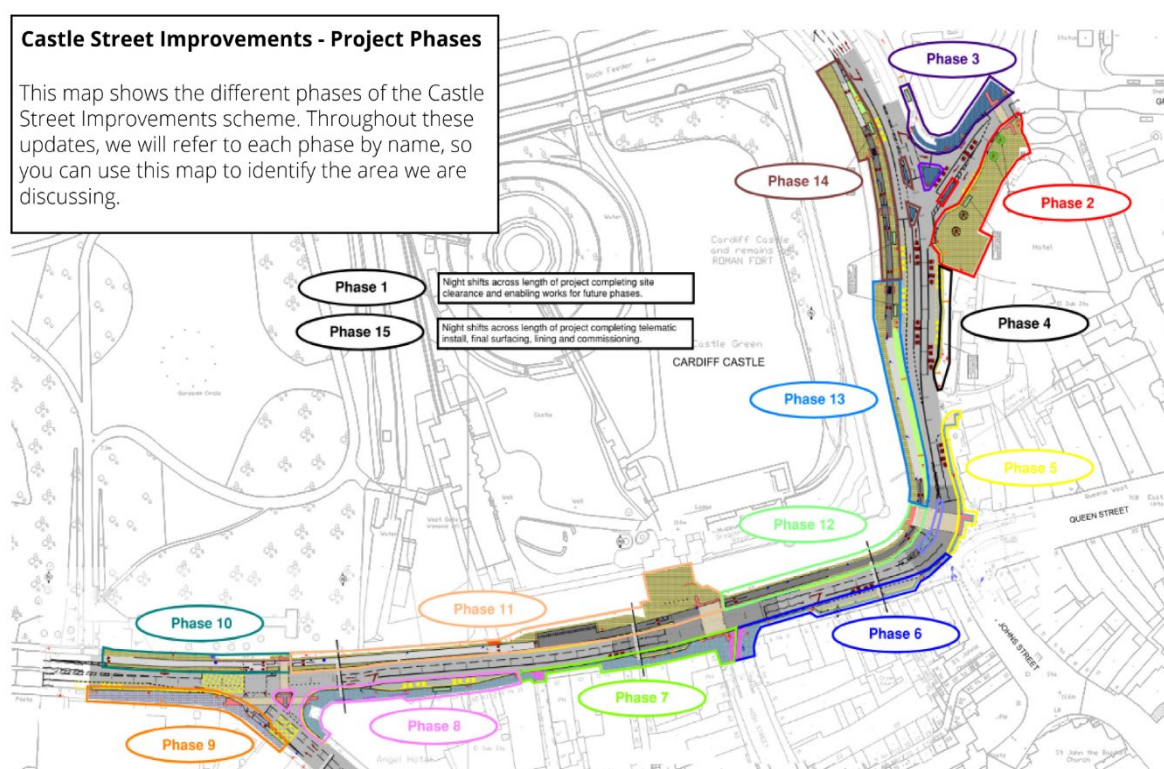

Phase 2

Work in this area will include:

- Installation of traffic signal ducting.
- Site clearance in preparation for slab laying.
- Installation of paving slabs.

- Base and binder surfacing works to be carried out by Tarmac on 23 and 24 July.

Phase 3

Work in this area will include:

- Installation of temporary traffic management on 27 July 2026.
- Trial hole investigations.
- Removal of existing traffic signals.

Phase 5

Work in this area will include:

- Installation of slabs and kerbs.
- Grouting works to the area.
- Completion of Phase 5 works.

Phase 6

Work in this area will include:

- Installation of drainage infrastructure.
- Full road construction works.
- Installation of highway kerbs.
- Excavation works for lighting columns.
- Preparation works for paving are due to commence towards the end of the week commencing 27 July.

Phase 8

Work in this area will include:

- Installation of drainage infrastructure.
- Full road construction works.
- Installation of highway kerbs.
- Installation of bus stop kerbs.
- Base and binder surfacing works to be carried out on 23 and 24 July.
- Phase 8 will be extended towards the Angel Hotel to allow excavation works to continue.

Minimising the Impact

We know construction works can be inconvenient at times, and we'd like to thank everyone for their continued patience while these improvements are carried out.

To help reduce disruption, we will continue to:

- Maintain clearly signed pedestrian routes and access to businesses and properties.
- Keep all work areas safely segregated from the public.
- Use appropriate measures to control noise and dust wherever possible.
- Carry out works during agreed working hours.
- Provide opportunities for feedback through the QR codes displayed around the site.

Get in Touch

If you have any questions or concerns about the Castle Street Improvements, please contact us:

Email: talktous@hotmail.co.uk

Public Liaison: 07977 091261

Thank you again for your continued support and patience as we deliver these important improvements for Cardiff city centre.

Next Update: Our next fortnightly e-bulletin will be issued Friday 7 August.
